

Prepared for



Commercial Proposal · Technical Architecture · Scope of Work

ERP Implementation Proposal

Phase 1 Production-Ready Operational ERP for Infra / EPC Project Execution.

Prepared by



Phase 1 · MVP

~6 months

2-3 week release cadence

Confidential · For evaluation by Unique Infra Engineers Pvt Ltd

A production-ready operational ERP, delivered release by release.

PHASE 1 DURATION ~6 months From kickoff to production go-live	RELEASE CADENCE Every 2–3 wks Working software, demoed each release	PHASE 1 COMMERCIAL ₹15,00,000 + GST Milestone-linked payments	SOURCE CODE Owned by Client after full payment
--	--	--	--

Objective Build a production-ready operational ERP for Infra / EPC project execution. A web-based, mobile-responsive system serving project, site, store, HR and management users — engineered for real users and real transactions from Day 1.	Phase 1 Focus Operational modules that run the project floor. Project execution · Procurement · Inventory & site stores · Subcontractors · Plant / fuel · HRMS & basic payroll · Documents · Approvals · Portals · Reports · Tally handover & export.	Delivery Model Release-wise, 2–3 weeks per drop. Each release lands a usable slice of the system on UAT for stakeholder review, then to production after sign-off.
--	--	---

Scope discipline Tender/bidding, full finance & accounting, client RA billing, real estate sales, customer portal, live statutory integrations and advanced analytics are explicitly Phase 2. Phase 1 is scope-controlled and engineered for go-live.
--

A contractor’s ERP — designed around how Infra/EPC work actually runs.

Client profile

Unique Infra Engineers Pvt Ltd

An Indian Infra/EPC contractor executing roads, bridges, industrial parks, warehouses and related infrastructure works — project-driven, multi-site, document-heavy and asset-intensive.

Typical sectors served

 Roads & Highways

 Bridges & Flyovers

 Industrial Parks

 Warehouses

 Related Infra Works

Operating realities the ERP must respect

Project-wise execution with central oversight

Mixed centralized and project-wise procurement

Distributed site stores with daily material movement

Subcontractor-led work fronts, with deductions & recoveries

Owned + hired machinery, fuel tracked at site

Labour, HR and compliance documents at each site

ERP objective

Tighten operational control across every project, every site, every transaction.



Project-wise visibility

A single source of truth for cost, progress and material across each project.



Approval discipline

Formal, role-based approvals with audit trail on every key transaction.



Inventory accuracy

Site-wise stock, issues, returns and transfers — reconciled, not estimated.



Subcontractor tracking

Work orders, measurements, bills and recoveries in one trail.



Machinery & fuel

Deployment, log books and fuel — accountable per asset and per site.



Management reporting

Dashboards and MIS rolled up from operational data, not spreadsheets.

Operational foundation first. Then extend.

Phase 1 · In scope now

Operational ERP Foundation

~6 months · ₹15,00,000 + GST · Source code to client on full payment

**Core Platform**

Multi-company · roles · approvals · audit

**Procurement**

PR · RFQ · comparison · PO

**Subcontractor Mgmt**

WO · measurement · bills · recoveries

**HRMS / Basic Payroll**

Attendance · leave · expenses · payroll

**Vendor / Subco Portals**

Basic, operational portals

**Reports & Dashboards**

Operational MIS · exports

**Project Execution**

WBS · DPR · progress · registers

**Inventory / Site Stores**

GRN · issue · return · transfer · ledger

**Plant / Machinery / Fuel**

Master · log book · fuel · maintenance

**Document Management**

Repo · tags · access · expiry

**Tally Export**

Accounts handover-ready

**Access & Audit**

RBAC · approvals · audit trail

Phase 2 · Roadmap

Advanced & Extended Modules

Scoped & priced separately after Phase 1 go-live

**Tender & Bidding**

Pre-bid management, BOQ build-up, estimates

**Client RA Billing**

Running account & government billing formats

**Customer Portal**

External-facing client & buyer interface

**Advanced Analytics & Integrations**

Forecasting, BI, third-party connectors and external system integrations

**Full Finance & Accounting**

Ledger, trial balance, P&L, balance sheet

**Real Estate Sales**

Inventory, bookings, collections

**Statutory Integrations**

Live e-invoice, e-way bill, GST APIs

Twelve modules, one operational backbone.

#	MODULE	PHASE 1 SCOPE
01	Core Platform	Multi-company / SPV / JV, users, roles, permissions, approvals, audit trail
02	Masters	Company, project, site, vendor, subcontractor, employee, item, equipment, WBS / cost codes
03	Documents	Upload, tag, categorize, access control, expiry reminders
04	Project Controls	Project setup, WBS / cost codes, basic BOQ / budget baseline, DPR, progress, hindrance / claim / variation registers
05	Procurement	PR / MR, RFQ, quotations, comparison, PO, approvals, PO PDF
06	Inventory / Site Stores	GRN, basic QC, stock ledger, issue, return, transfer, adjustment
07	Subcontractors	Work order, measurement / progress, bill tracking, deductions / recoveries, portal
08	Plant / Fleet / Fuel	Equipment master, deployment, log book, fuel consumption, basic maintenance
09	HRMS	Employee master, attendance, leave, basic payroll, expenses, labour attendance & compliance docs
10	Portals	Basic vendor and subcontractor portals
11	Reports	Operational MIS, dashboards, Excel / PDF exports
12	Tally Handover	GST / TDS data capture & export, vendor / subcontractor bills, expense / payroll export

Note · All twelve modules are delivered release-by-release over the ~6 month Phase 1 window. See Slide 18 for the detailed release plan.

One platform. Many companies, projects and roles.

Capabilities

**Multi-company / SPV / JV**
Single platform, multiple legal entities

**Company & project-wise access**
Users see only what they should

**Role-based access control**
Granular permissions per role

**3-4 level approval workflow**
Fixed, auditable approval chain

**Revise / cancel with audit**
Approved records protected, history kept

**Master Excel import / export**
Onboarding-friendly data setup

**Transaction audit trail**
Who did what, when

**Internal notifications**
Basic alerts on pending actions

Approval workflow · Up to 3-4 levels

Every key transaction passes through a defined approval ladder.

L1

Initiator / Maker
Creates the transaction at site / project

L2

Project / Functional Review
Verifies scope, quantity, vendor, budget

L3

HO / Commercial
Confirms rate, terms, compliance

L4

Management Approval
Final release · Audit-locked thereafter

Approved transactions can only be revised or cancelled through a controlled flow — original entry, approver and reason are retained in audit history.


A single, controlled repository for every document the project floor handles.

Capabilities

- **Centralized repository**
Every document accessible from one place
- **Linked to transactions**
Project · vendor · subcontractor · employee · equipment · PO · WO · GRN · invoice / bill
- **Categories & tags**
Organised retrieval at scale
- **Role / company / project access**
Visibility controlled at every layer
- **Expiry tracking**
Reminders for licences, insurances, compliance docs
- **Upload history & audit trail**
Who uploaded, when, and what changed

Repository structure

Documents linked to the entities they belong to.

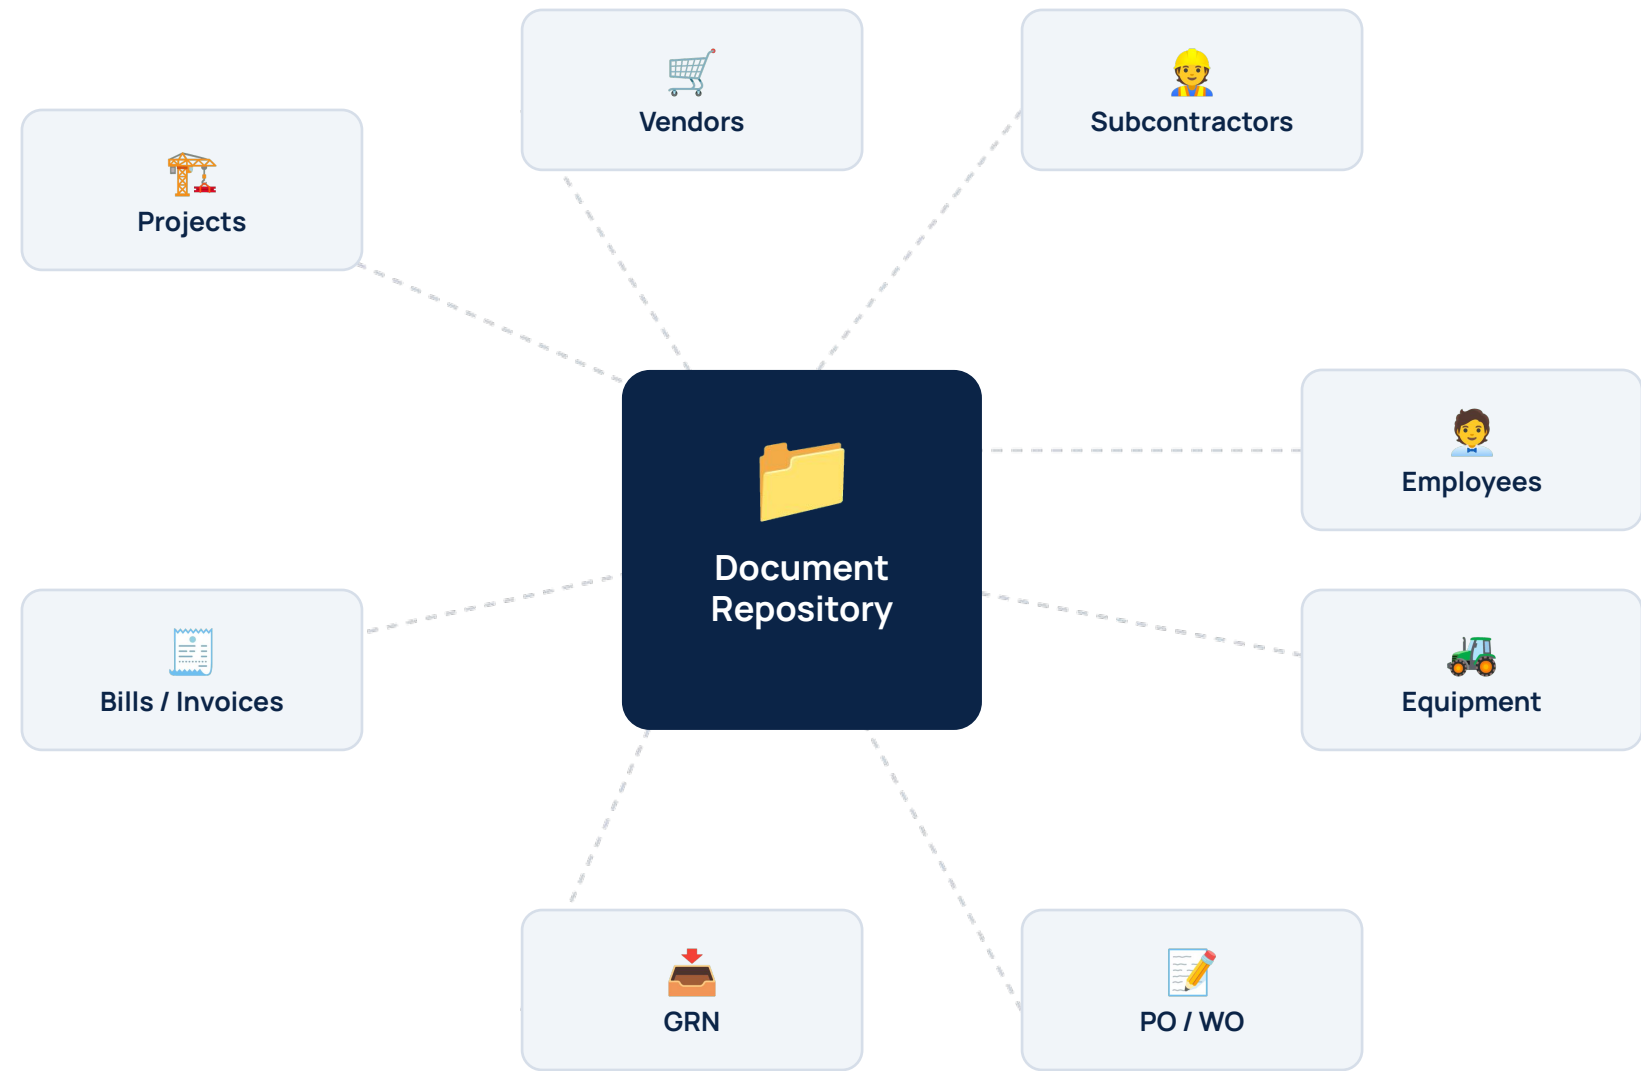

From contract summary to daily progress – every project under control.


 Project setup & baseline	 Daily execution capture	 Registers & tracking
Project master & contract summary WBS / cost code setup Basic project BOQ & budget baseline Budget revision with approval Project dashboard at a glance	Daily Progress Report (DPR) Quantity progress tracking Manpower usage capture Machinery usage capture Material usage capture	Hindrance / delay register Variation / claim / escalation registers BG / security deposit / retention register — basic Linked documents on every register entry Status & ageing visibility

Phase 1 boundary ·

Client RA billing and full government billing formats are **not** included in Phase 1 — these are planned for Phase 2.

From requisition to handover – one auditable trail.

End-to-end workflow

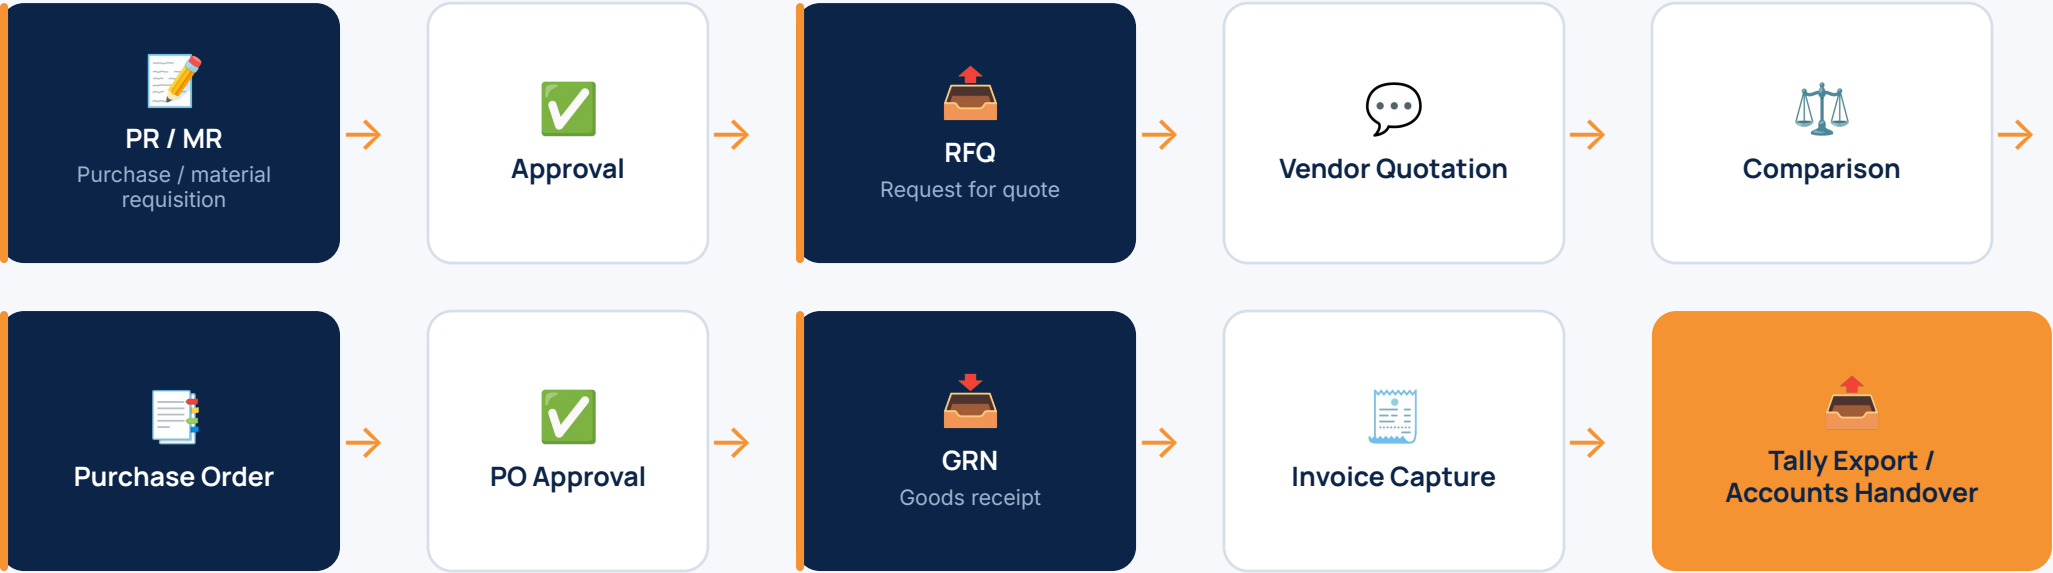

Key features

Project-wise & centralized Both modes supported	Vendor quotation entry Manual or portal-submitted	PO generation & approval PO PDF auto-generated	Basic PO revision Amendment with audit history	Purchase invoice capture Ready for accounts export
---	---	--	--	--

Site-wise stock, reconciled to the last issue.

Stock movement flow

Inward · Internal · Outward

► Inward

Opening stock import → GRN against PO → Basic QC / acceptance → Site-wise / store-wise stock

► Issue & return

Issue → WBS Issue → Project Issue → Subcontractor Issue → Equipment Material return

► Internal movements

Site-to-site transfer Store-to-store transfer Stock adjustment (with approval)

► Visibility

📖 Stock ledger

Per item, per site — full movement history

📊 Material reconciliation (basic)

Issue vs consumption

Stock snapshot (illustrative)

Live across sites & stores.


ITEM	SITE	STOCK	UOM
OPC 53 Cement	Site-A	1,240	Bags
TMT Bar 16mm	Site-A	38.6	MT
Aggregate 20mm	Site-B	420	CuM
M-Sand	Site-B	95	CuM
HSD Fuel	Site-A	2,860	L
Shuttering Ply 12mm	Central	160	Nos
Bitumen VG-30	Site-C	14.2	MT

Reporting

Excel exports PDF reports Stock summary Material issue report

Onboarding to bill – every recovery captured, every deduction visible.

End-to-end subcontractor workflow

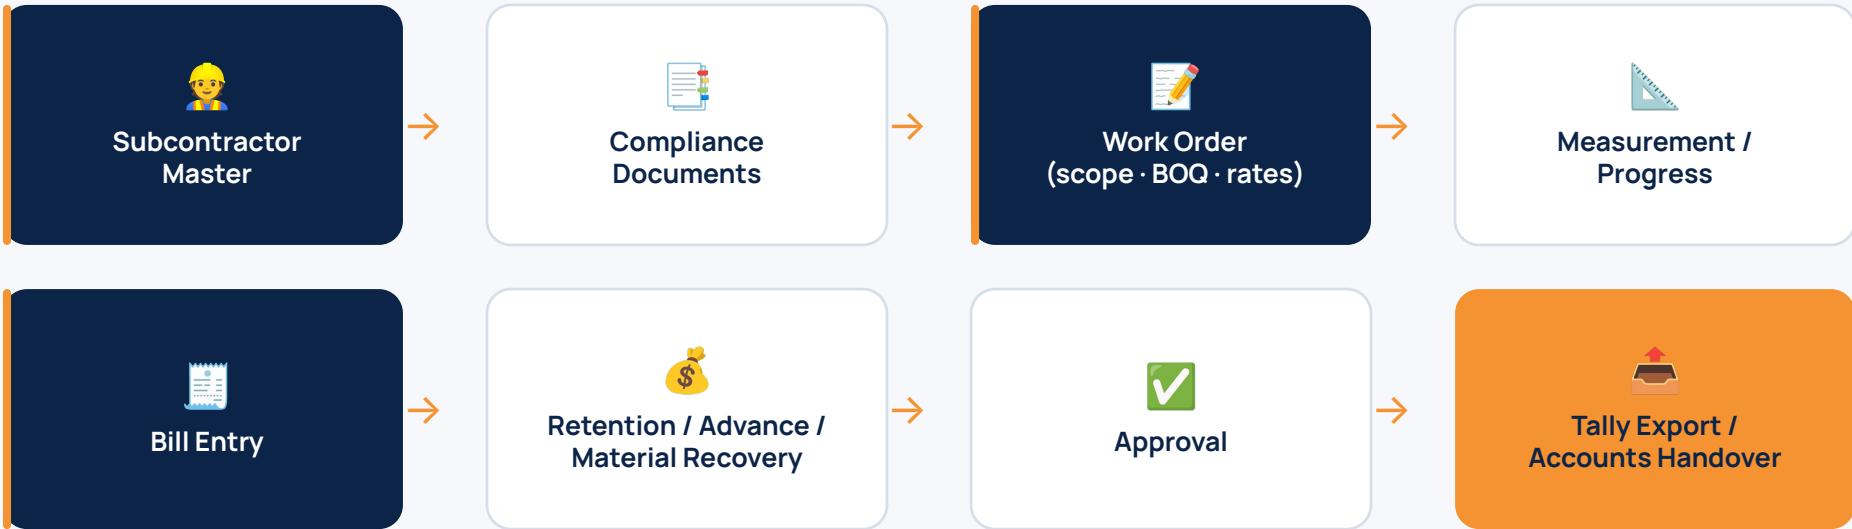

Feature highlights

Built for site reality.

- Subcontractor onboarding with KYC & documents
- Work order with scope, BOQ & rates
- Measurement / progress entry per WO line
- Bill status tracking — entered, approved, exported
- TDS / GST data capture for export
- Deductions: retention, advance recovery, material recovery
- Basic subcontractor portal for self-service

Bill journey: entered at site → reviewed by project → approved at HO → exported to accounts. Every step is logged.

Asset deployment, daily log, and fuel – accountable to the meter.

Master & deployment	Daily operations	Maintenance & reports
 Asset register Equipment / vehicle master Owned vs hired classification Deployment to project / site Operator / driver allocation Asset documents & insurance Outcome Every machine has an owner, a site and a deployment status — at all times.	 Log book & fuel Daily log book entries KM / hour meter readings Fuel issue at site Fuel consumption tracking Basic fuel efficiency comparison Outcome Fuel issued at site is tied to the asset that consumed it — leakage gets noticed.	 Uptime control Breakdown entry & downtime capture Basic preventive maintenance schedule Service / repair log Equipment utilisation reports Fuel consumption & efficiency reports Outcome Preventive schedules surface upcoming services before breakdowns hit progress.

Staff, labour and site expenses – under one roof.



Pillar 1

Employee & payroll


- Employee master with documents
- Project / site allocation
- Attendance — manual entry / import
- Leave tracking
- Basic payroll calculation
- Salary advance & recovery
- Payroll summary export for accounts / Tally



Pillar 2

Expenses & travel

- Expense claims with documents
- Travel & reimbursement claims
- Project / site allocation per claim
- Approval workflow on claims
- Status tracking through to export
- Export ready for accounts handover



Pillar 3

Contractor labour

- Contractor labour attendance
- Per-site, per-contractor head count
- Labour compliance document tracking
- Document expiry reminders
- Site-wise labour visibility

Phase 1 boundary ·

Full statutory payroll return formats — advanced PF / ESI / PT / TDS reports — are planned for **Phase 2** unless separately scoped.

External actors, brought inside the workflow.

Vendor Portal

 For suppliers & material vendors

**Secure login**
Each vendor, individually credentialed

**Document upload**
KYC, licences, certificates

**Submit quotation**
Directly against an RFQ

**View GRN / invoice status**
Basic status visibility — entered, approved, exported

**Profile view / update**
Change requests, not direct edits

**View RFQs**
Issued by procurement

**View PO**
PO PDF accessible from portal

Subcontractor Portal

 For work-front subcontractors

**Secure login**
Per-subcontractor credentials

**View work orders**
Scope, BOQ and rates

**View bill & payment status**
Basic status — entered, approved, exported

**Profile & documents**
Compliance docs, licences

**Upload bills / supporting docs**
Against a specific WO

Phase 1 scope note ·

Portals in Phase 1 are **basic and operational** — not advanced collaboration platforms. Advanced features sit in Phase 2.

Numbers that decision-makers actually open.

Reports & Dashboards

 Operational MIS at every level

► Dashboards

 Management

 Project

 Procurement

 Inventory

► Reports

 PR pending

 PO register

 GRN register

 Stock summary

 Stock ledger

 Material issue

 Subco WO / bills

 Equipment / fuel

 Attendance / payroll

 Document expiry

 Project dashboard data

 Export logs

► Output formats

 Excel

 PDF

 On-screen dashboard

Tally / Accounts handover

 Bridge to your accounts team.

Vendor / subcontractor master export

Purchase invoice export

Subcontractor bill export

Expense claim export


Payroll summary export

GST / TDS data export

Export log & status (what went out, when)

Phase 1 boundary · Full finance & accounting — trial balance, P&L, balance sheet, bank reconciliation, payment accounting — sit in **Phase 2**. Phase 1 generates accounts-ready exports.

A modern, production-grade stack — engineered for real users.

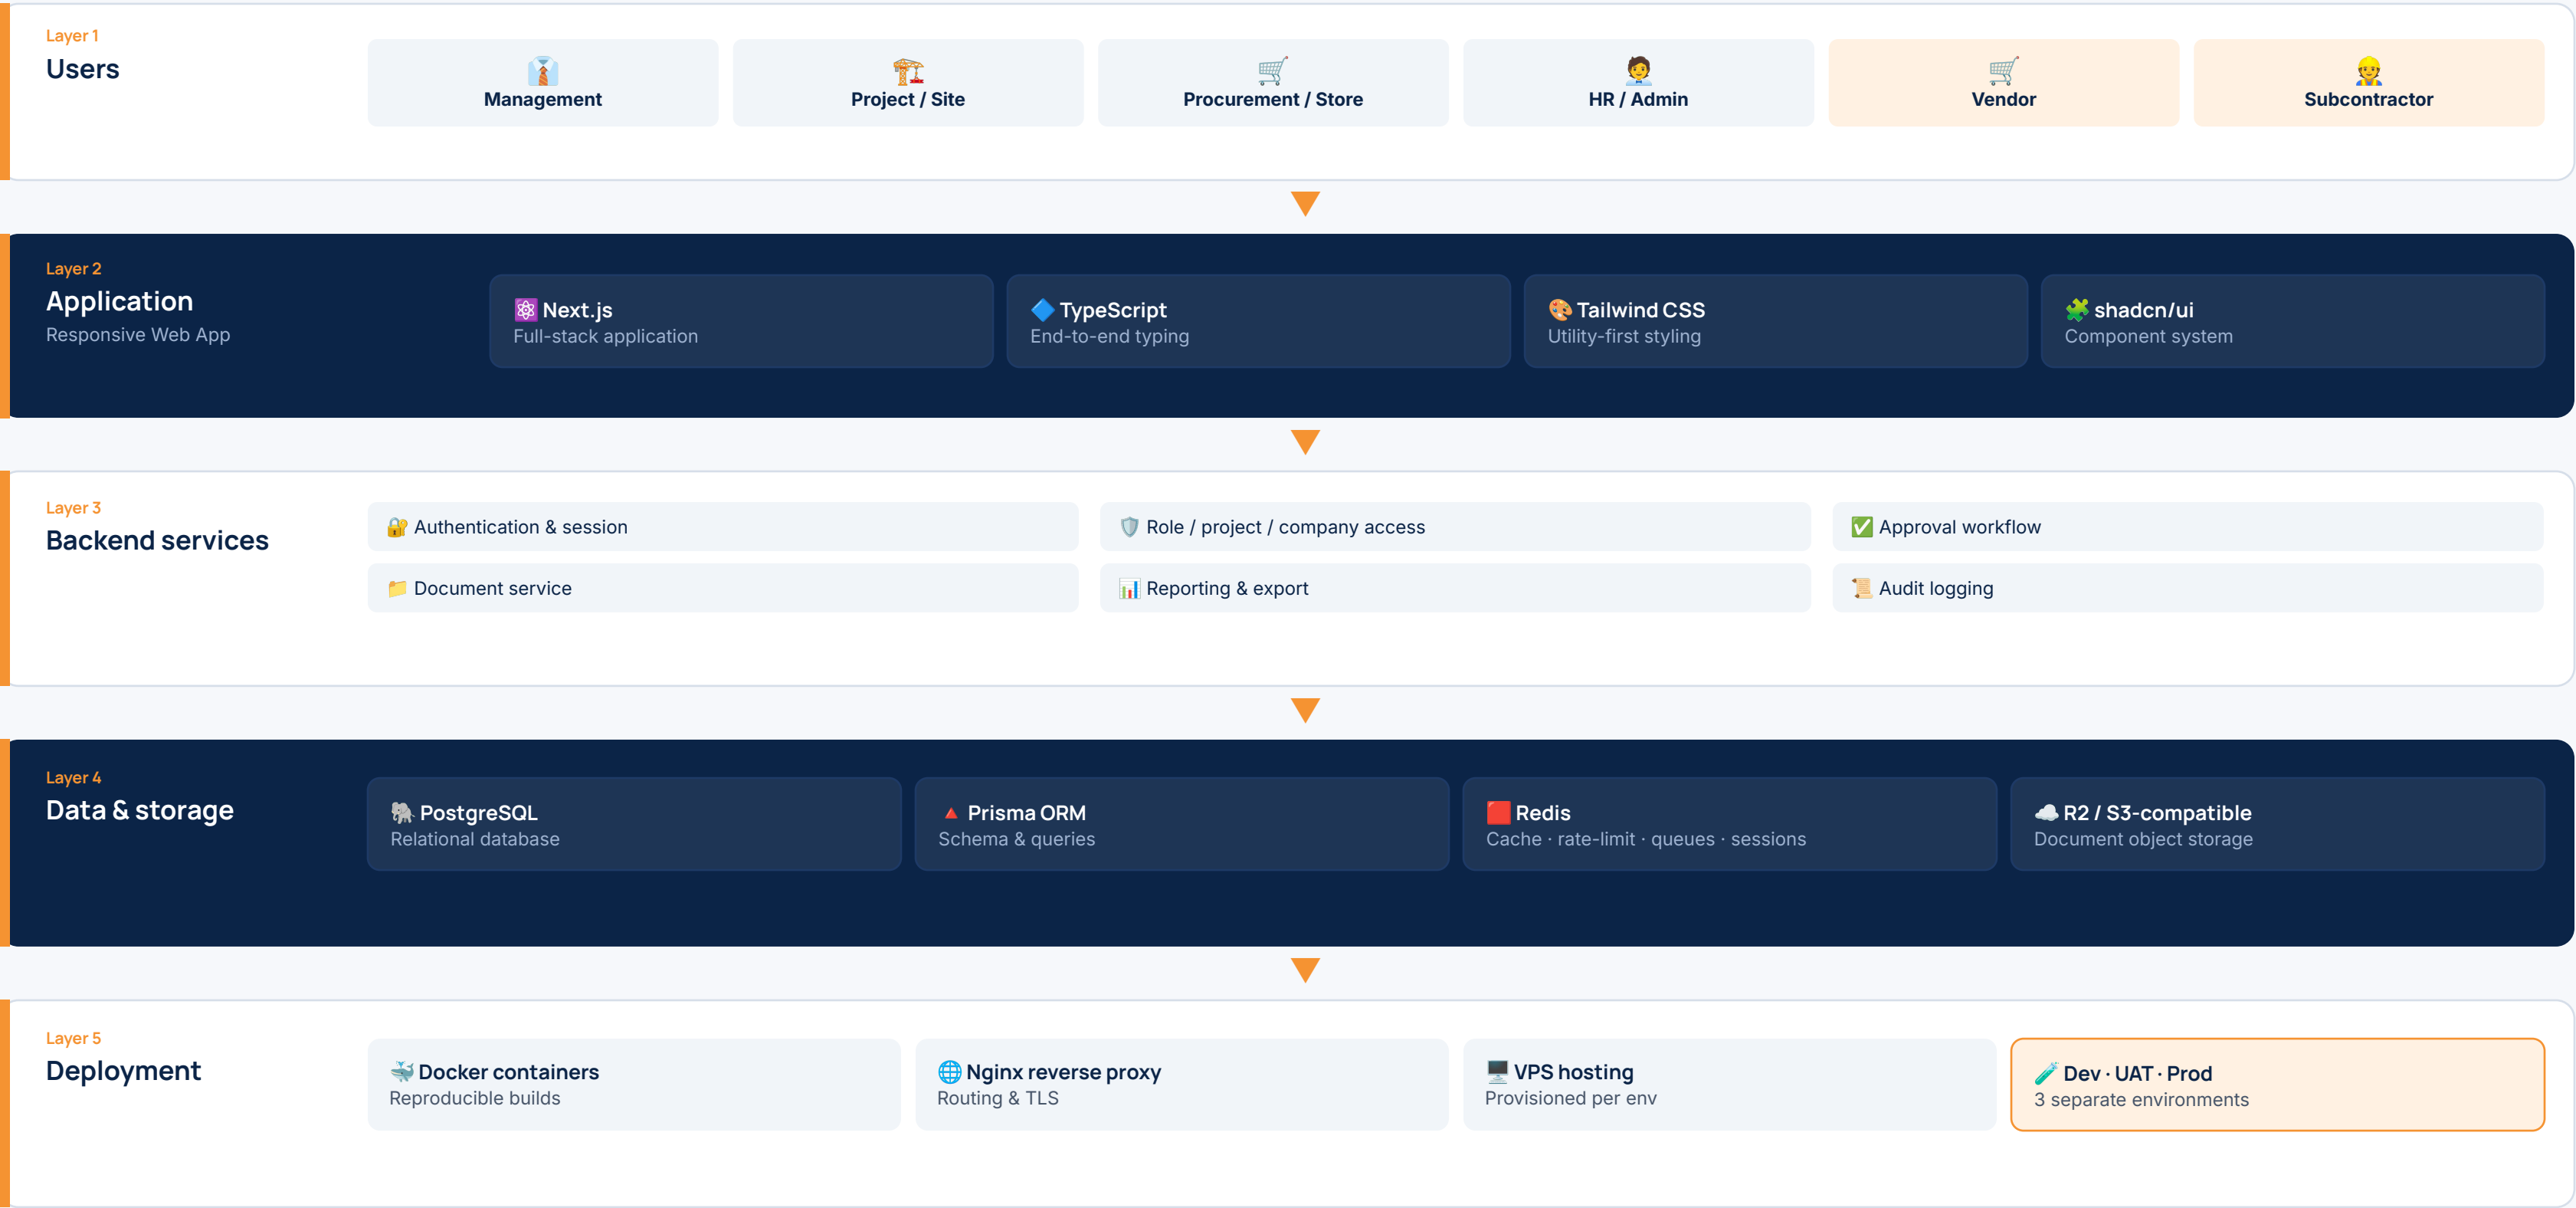

Architecture note · Each layer is decoupled — services can be scaled, replaced or upgraded independently as load grows.

Hardened by design. Audited by default.

Pillar 1  Access & identity	Pillar 2  Audit & integrity	Pillar 3  Abuse prevention	Pillar 4  Deployment controls
Secure email & password authentication Industry-standard password hashing Login attempt lockout HTTPS across all environments Role-based access control Company-wise & project-wise permissions	Transaction audit trail on key entries Approved transactions protected from silent editing Revision / cancellation flow with reason & approver Who-did-what visibility on every record Document upload history	Rate limiting on sensitive endpoints Account lockout against brute-force attempts Server hardening & firewall configuration Access-controlled file storage Environment isolation across dev / UAT / prod	Separate dev / test / production environments Containerised, reproducible deployments Backup planning HTTPS-only access via reverse proxy Controlled release process per milestone

In plain words

Account lockout helps prevent brute-force login attempts. Rate limiting and server hardening reduce broader abuse. Once a transaction is approved, no one can silently edit it — every change is captured in the audit history.
